
KIMBALL MAIN STREET ROADWAY AND UTILITY IMPROVEMENTS


PERCENT COMPLETE: 76%

PROJECT DESCRIPTION

This project includes watermain and sanitary sewer replacement, complete street reconstruction, concrete driveway, pedestrian ramp, and sidewalk replacement. Construction is expected to be completed at the end of November or early December, weather permitting.

PROJECT UPDATE | November 16th, 2026

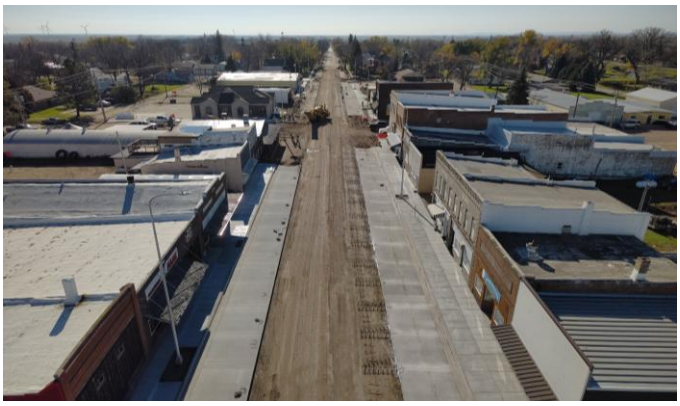

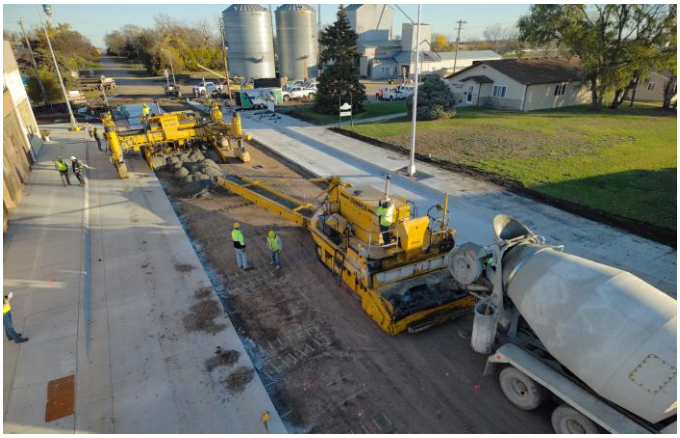



PROJECT INFORMATION

CONSULTANT:
Banner Associates, Inc.
3900 N Northview Ave, Sioux Falls, SD 57107
855-323-6342 (toll free)
CONTACT: Spencer Gilk

CONTRACTOR:
SiteWorks, Inc
4825 N Wilcox Dr, Sioux Falls, SD 57104
(605) 400-0458
CONTACT: Jeff Haas

OWNER:
Kimball
140 Main Street, Kimball, SD 57355
(605) 778-6277
CONTACT: Lydia Morley | Bill Gough

PROJECT UPDATE AND SCHEDULE

- Roadway Reconstruction and Surfacing
  - Mainline sidewalk installation Railroad to 3rd Street is 90% complete
  - Base course was cut to final grade prior to concrete paving.
  - West driving lane is complete
- Upcoming work
  - East driving lane will be paved
  - On side streets, roadway base course preparation and compaction will continue until required stability is achieved. Base course will be cut to final grade prior to asphalt paving.
  - Intersection bumpouts, sidewalk, and curb and gutter will be completed after concrete paving.
  - Sidewalk installation will continue where curb and gutter is installed.
  - Side street asphalt pavement installation will begin after concrete paving is complete, weather pending.
  - Joint sealing, lane and parking striping will begin after paving is complete.

BANNER
engineering a better community
